

Chemung County Stormwater
Construction Inspection
Erosion and Sediment Control



Project Name LECOM	Date 11-14-2019
Location Park Ave Elmira (City), NY	Permit # NYR11E617
Weather Conditions overcast, cold	Entry Time: 9:02 am
On-Site Representative Present: Brian Atwater	Exit Time: 9:48 am

Construction Site Notes:

	-Project is near completion. Parking area is completed. Landscaper is working to stabilize all bare soil areas with sod.

Yes	No	N/A	
		X	All erosion and sediment control measures installed/constructed
		X	All erosion and sediment control measures maintained properly
	X		Are there currently more than 5 acres disturbed w/o prior approval
X	X		Have stabilization measures been initiated in inactive areas
X			Are permanent stormwater control measures being implemented
	X		Was there a discharge into the receiving water on the day of inspection
	X		Evidence of turbidity or oil in the receiving waters
X			Are weekly inspections being performed?
X			Are the inspections being performed by a qualified individual?


Corrections Needed:

-Silt fence has been removed from the project perimeter. In areas along Clinton Street and Park Place the soil has not yet been stabilized. It is getting tracked onto municipal roads. Sweeping sediment out of street is required.

-North-east water quality unit is not sitting correctly. The pipes are not straight up and down. There is concern it is not aligned with the stormwater pipe correctly. Also, it is not grouted around the unit.

Satisfactory Marginal x Unsatisfactory

Date 11/14/19	Inspector Jessica Verrigno
----------------------	-----------------------------------



COUNTY OF CHEMUNG
Chemung County Stormwater Coalition
851 Chemung Street
Horseheads, New York 14825
Ph. 607.796.2216

PROJECT: LECOM
City of Elmira
Municipal Construction Inspection
November 14, 2019

BY: Jessica Verrigni, CPESC, CPSWQ




Erosion controls removed along Clinton Street. Sediment is being tracked into the road.



Erosion controls along Park Place have been removed. Equipment is tracking sediment into the road.



North-east water quality unit is not sitting straight up and down. It has also not been grouted correctly.

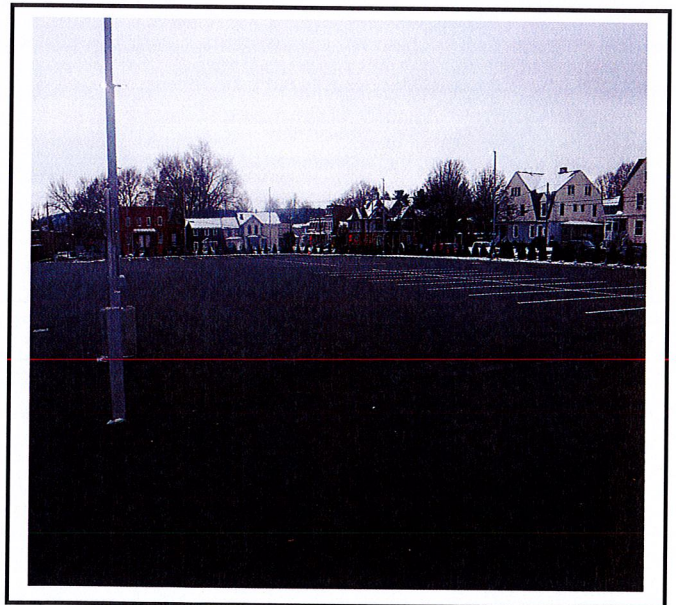

Completed parking lot where underground stormwater infiltration and water quality units are located.
