

**Chemung County Stormwater
Construction Inspection
Erosion and Sediment Control**



Project Name Barrington West Lot 54	Date 6-28-2022
Location Royal Crest Horseheads, NY	Permit # NYR11F212
Weather Conditions sunny warm	Entry Time: 10:26 am
On-Site Representative Present: Roz Steadman	Exit Time: 10:50 am

Construction Site Notes:

-Spoke with developer on site. Waiting for Will Wood to come back and finish electric and plumbing lines into home. When he does that he will rough grade the site and they will get it stabilized. Roof gutters will be in by then too. Majority of roofs will flow out to front.

Yes	No	N/A	
x			All erosion and sediment control measures installed/constructed
	x		All erosion and sediment control measures maintained properly
		X	Are there currently more than 5 acres disturbed w/o prior approval
	x		Have stabilization measures been initiated in inactive areas
		X	Are permanent stormwater control measures being implemented
	X		Was there a discharge into the receiving water on the day of inspection
	X		Evidence of turbidity or oil in the receiving waters
X			Are weekly inspections being performed?
X			Are the inspections being performed by a qualified individual?

Corrections Needed:

-Erosion occurring around the entire property because nothing is stabilized. Silt fenced are capturing the sediment. See not above on when this will be corrected.

Satisfactory Marginal Unsatisfactory x

Date 6/28/22 **Inspector** *Jessica Verrianni*



COUNTY OF CHEMUNG
Chemung County Stormwater Coalition
851 Chemung Street
Horseheads, New York 14825
Ph. 607.796.2216

PROJECT: Barrington West Lot 54
Town of Horseheads
Municipal Inspection
June 28, 2022


BY: Jessica Verrigni, CPESC, CPSWQ



Erosion occurring at rear of property.



Silt fence not toed in where electric line needs to be buried.

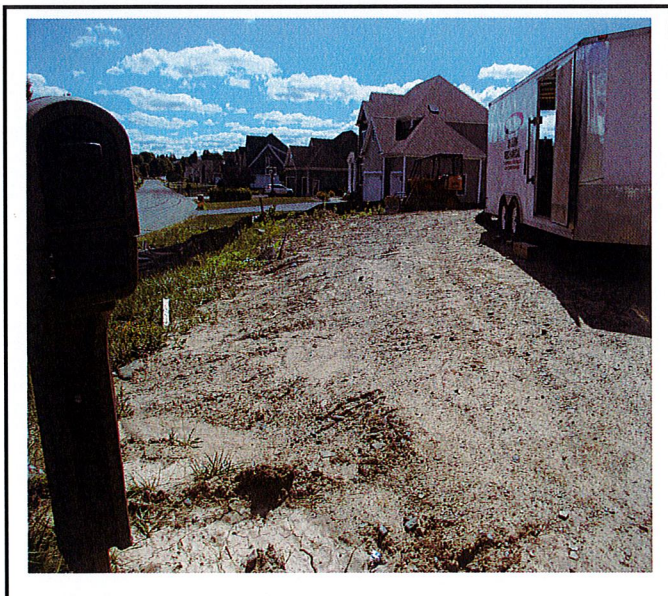

Bare compacted soil is eroding due to lack of stabilization.

